















Project: GDFR_Initial_Schedule Date: Wed 9/13/06	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	

ID	Task Name	Duration	Start	September						October				Nov
				8/20	8/27	9/3	9/10	9/17	9/24	10/1	10/8	10/15	10/22	10/29
33	DLF	3 days	Wed 11/8/06											
34	Nov 13-30	14 days	Mon 11/13/06											
35	design network configuration policies	4 days	Mon 11/13/06											
36	prototype LOCKSS distribution	7 days	Fri 11/17/06											
37	prototype release and report	3 days	Tue 11/28/06											
38	prototype registry manager	8 days	Mon 11/13/06											
39	December timebox	23 days	Fri 12/1/06											
40	design inter-nodal authentication	4 days	Fri 12/1/06											
41	submit article about GDFR to DLF	3 days	Thu 12/7/06											
42	publish full specs	1 day	Tue 12/12/06											
43	publish article for DLIB	4 days	Wed 12/13/06											
44	repository integration test design	5 days	Tue 12/19/06											
45	define operations/stats requirements	5 days	Tue 12/26/06											
46	implementation platform defined	1 day	Fri 12/1/06											
47	implementation plan completed	6 days	Tue 12/26/06											
48	2nd invoice (complete specs & implementati	0 days	Tue 1/2/07											
49	registry UI design	10 days	Fri 12/1/06											
50	Jan-March 2007, Implementation	60 days	Mon 1/1/07											
51	refactor prototype as needed	15 days	Mon 1/1/07											
52	build/deploy authentication	21 days	Mon 1/1/07											
53	build UI config for inter-nodal policies	20 days	Tue 1/30/07											
54	build registry UI	25 days	Mon 1/22/07											
55	add subscribe/notify to inter-nodal logic	10 days	Tue 2/27/07											
56	integrate repository core	20 days	Mon 2/26/07											
57	April-June 2007, Interim Release	53 days	Mon 4/2/07											
58	implement operations/stats	11 days	Mon 4/2/07											
59	production packaging	15 days	Mon 4/2/07											
60	documentation for interim release	3 days	Mon 4/2/07											
61	reference model code interim release	5 days	Thu 4/5/07											
62	deploy/configure QA test envs	15 days	Thu 4/12/07											
63	QA test cycle at OCLC	20 days	Thu 5/3/07											
64	OCLC inter-nodel testing & bug fixing	10 days	Thu 5/31/07											

Project: GDFR_Initial_Schedule Date: Wed 9/13/06	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	

ID	Task Name	Duration	Start	September						October				Nov
				8/20	8/27	9/3	9/10	9/17	9/24	10/1	10/8	10/15	10/22	10/29
65	 July-Sept 2007, Harvard test cycle	66 days	Mon 7/2/07											
66	2nd code refactor, bug fix	16 days	Mon 7/2/07											
67	2nd QA test cycle at OCLC	10 days	Tue 7/24/07											
68	3rd invoice (initial production release)	1 day	Tue 8/7/07											
69	Harvard initial install	14 days	Wed 8/8/07											
70	initial populate by Harvard staff	10 days	Tue 8/28/07											
71	Harvard inter-nodal testing	15 days	Tue 9/11/07											
72	 Oct-December 2007, Pre-release	52 days	Mon 10/1/07											
73	Iterative refactoring, bug fixing	30 days	Mon 10/1/07											
74	3rd QA test cycle at OCLC	22 days	Mon 11/12/07											
75	Pre-release planning	8.4 days	Mon 10/1/07											
76	 Jan-March 2008, Release	23 days?	Tue 1/1/08											
77	Turnover to external maintenance agent	15 days	Tue 1/1/08											
78	Final technical report	5 days	Tue 1/1/08											
79	 Open source available	1 day	Tue 1/15/08											
80	 Project end Jan 31, 2008	0 days	Thu 1/31/08											
81	4th invoice	1 day?	Thu 1/31/08											

Project: GDFR_Initial_Schedule Date: Wed 9/13/06	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	

November				December				January				February				March				April		
11/5	11/12	11/19	11/26	12/3	12/10	12/17	12/24	12/31	1/7	1/14	1/21	1/28	2/4	2/11	2/18	2/25	3/4	3/11	3/18	3/25	4/1	4/8

Abrams




Clark, Stanescu



TWG, Clark, Houser, Abrams, Stanescu




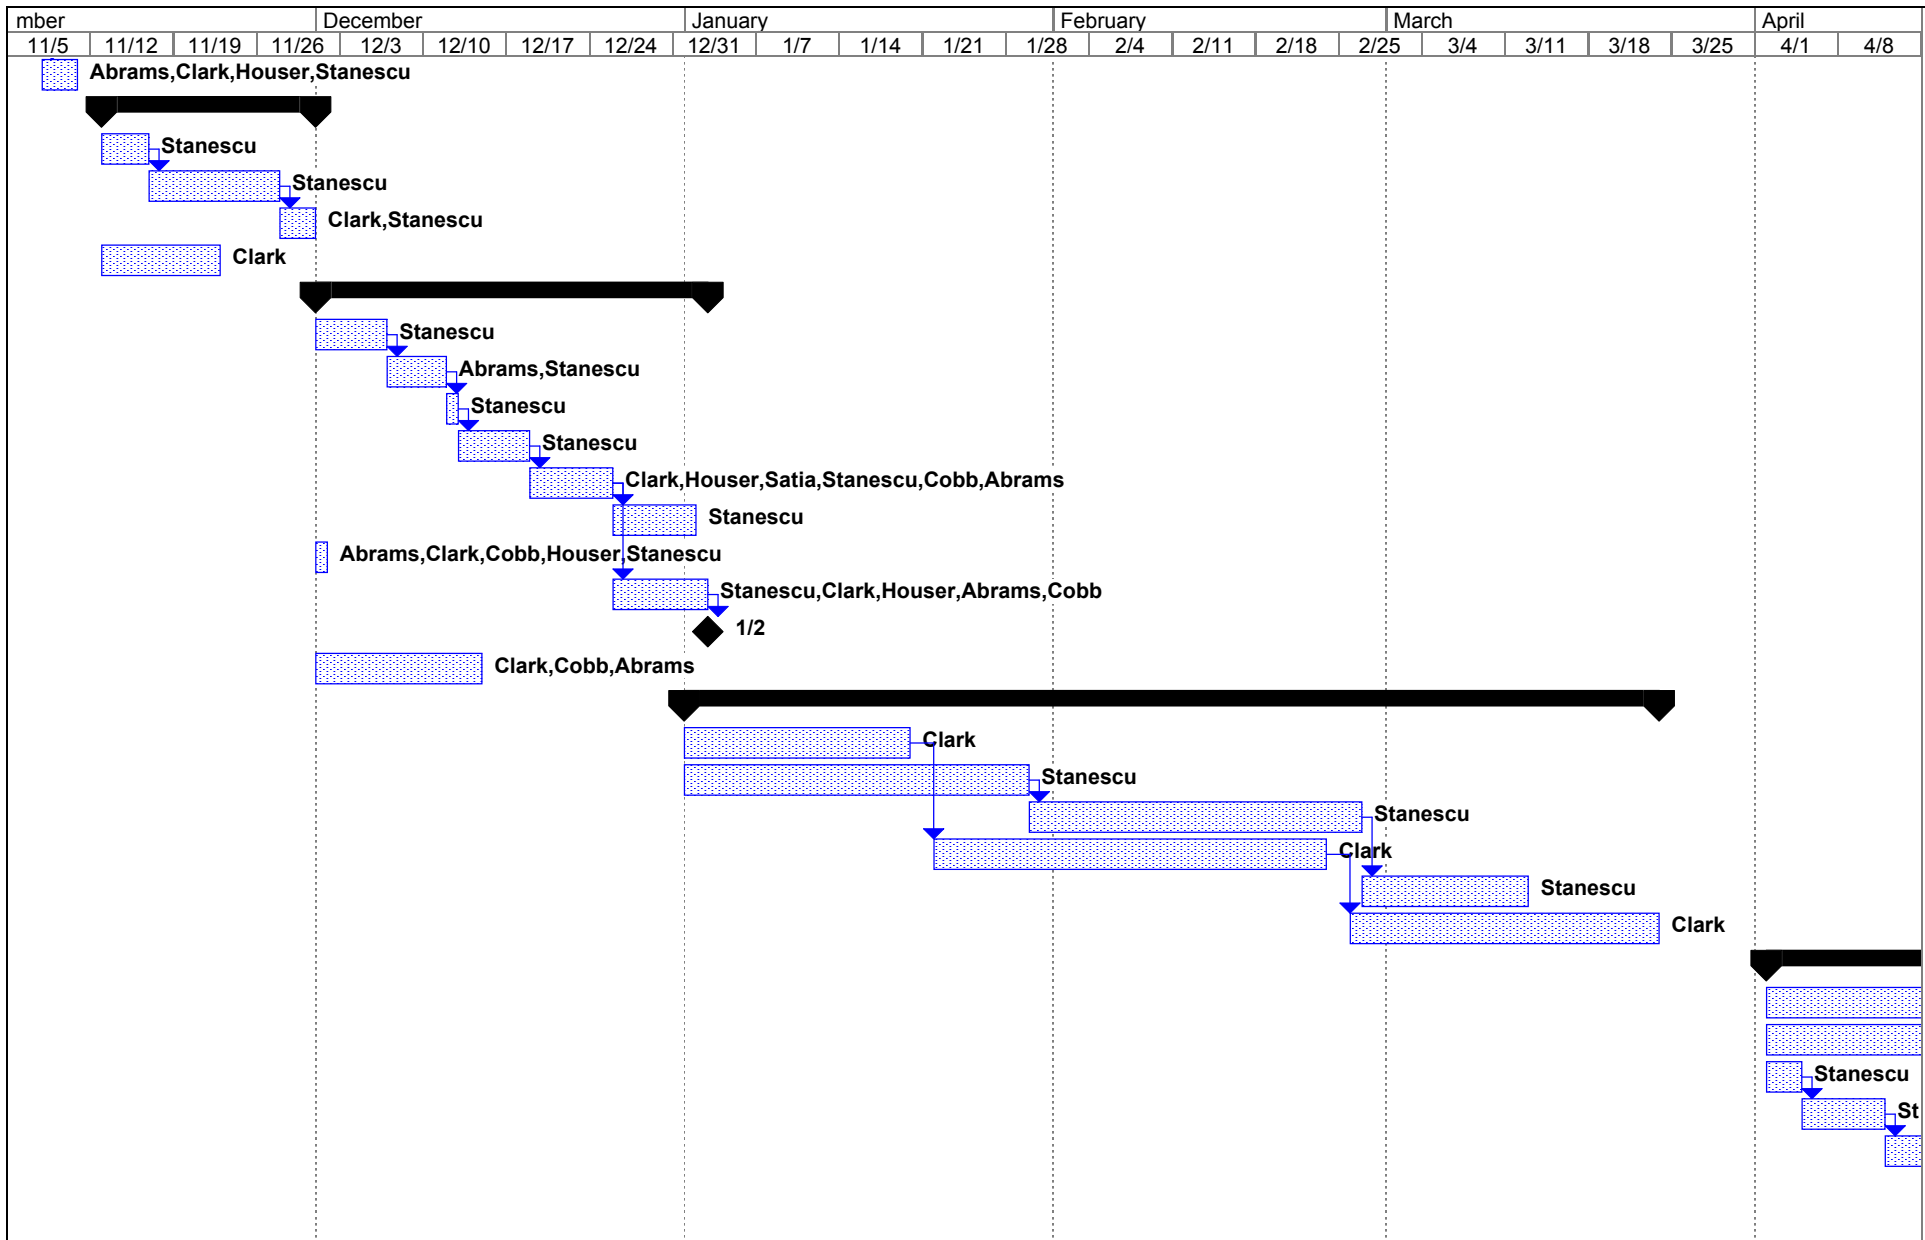





Project: GDFR_Initial_Schedule Date: Wed 9/13/06	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	












Project: GDFR_Initial_Schedule
 Date: Wed 9/13/06


Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

ember				December				January				February				March				April		
11/5	11/12	11/19	11/26	12/3	12/10	12/17	12/24	12/31	1/7	1/14	1/21	1/28	2/4	2/11	2/18	2/25	3/4	3/11	3/18	3/25	4/1	4/8


Project: GDFR_Initial_Schedule Date: Wed 9/13/06	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	

4/15			May				June				July				August				September			
4/15	4/22	4/29	5/6	5/13	5/20	5/27	6/3	6/10	6/17	6/24	7/1	7/8	7/15	7/22	7/29	8/5	8/12	8/19	8/26	9/2	9/9	9/16

Project: GDFR_Initial_Schedule Date: Wed 9/13/06	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	

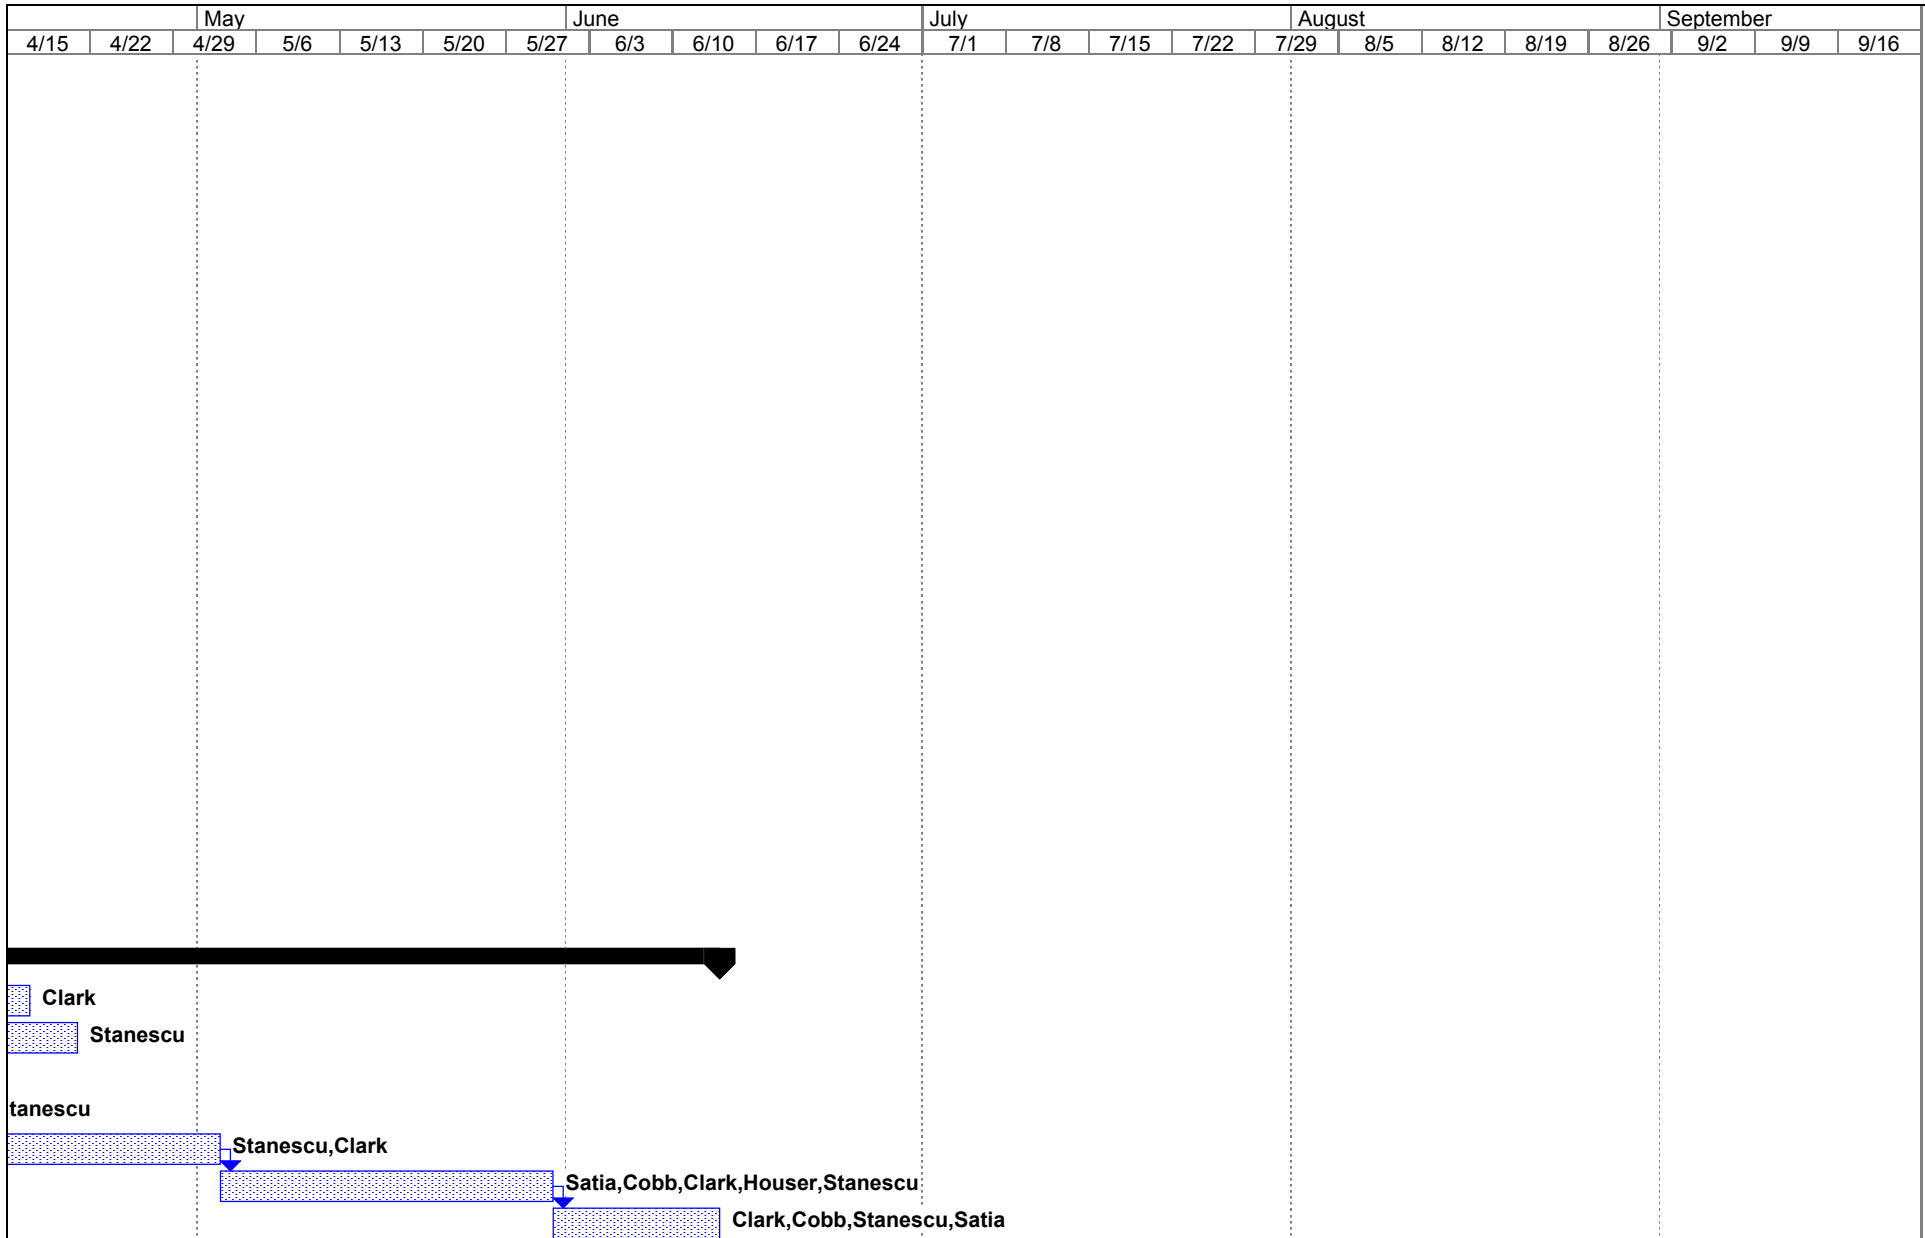




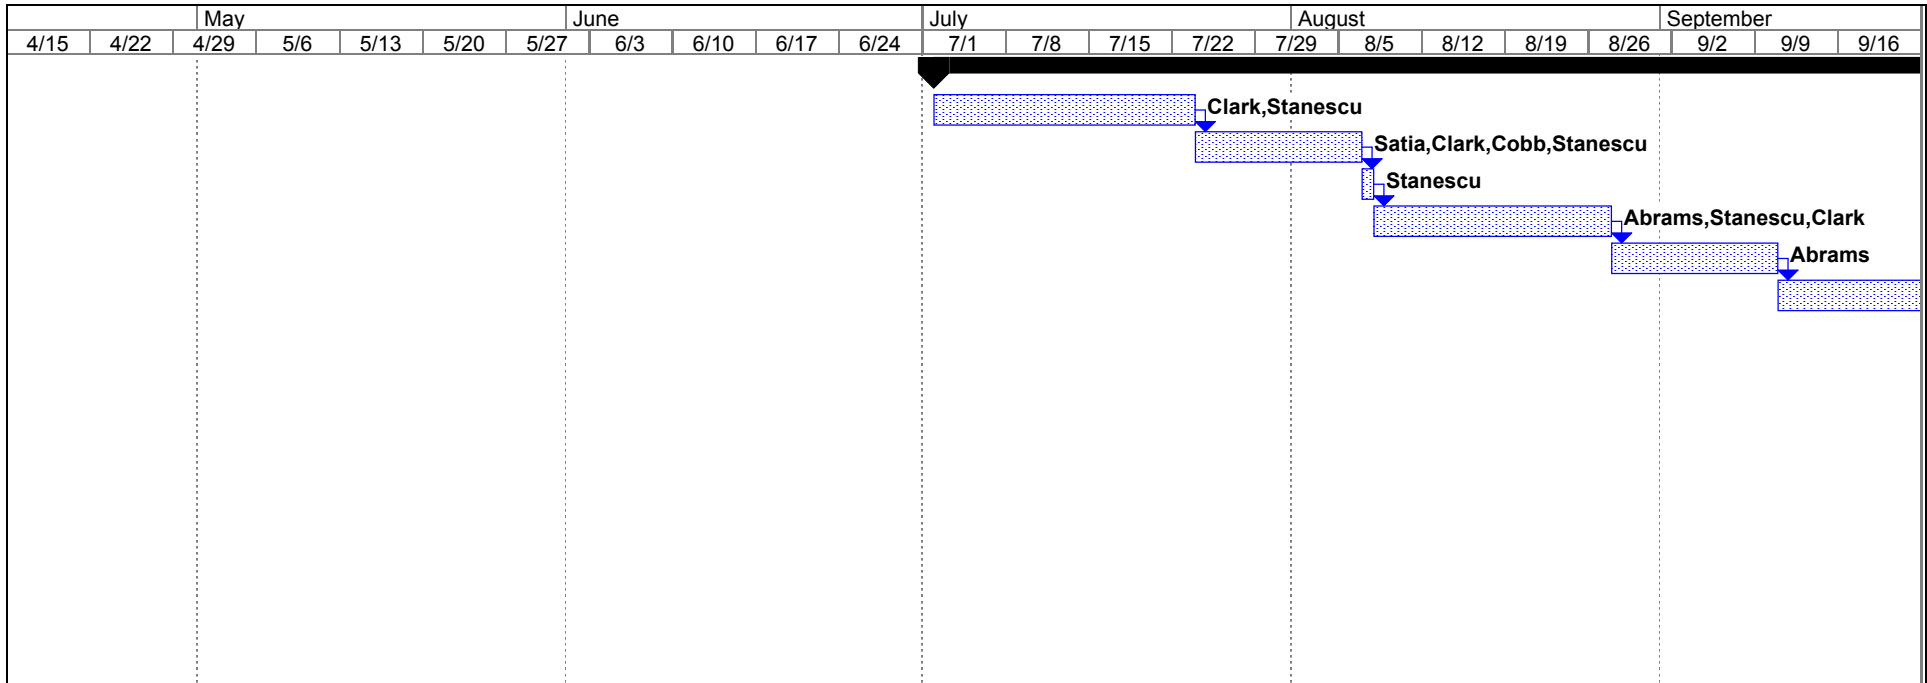





Project: GDFR_Initial_Schedule Date: Wed 9/13/06	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	













Project: GDFR_Initial_Schedule Date: Wed 9/13/06	Task	Milestone	External Tasks
	Split	Summary	External Milestone
	Progress	Project Summary	Deadline









	October					November					December				January				February			
9/23	9/30	10/7	10/14	10/21	10/28	11/4	11/11	11/18	11/25	12/2	12/9	12/16	12/23	12/30	1/6	1/13	1/20	1/27	2/3	2/10	2/17	2/24

Project: GDFR_Initial_Schedule Date: Wed 9/13/06	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	

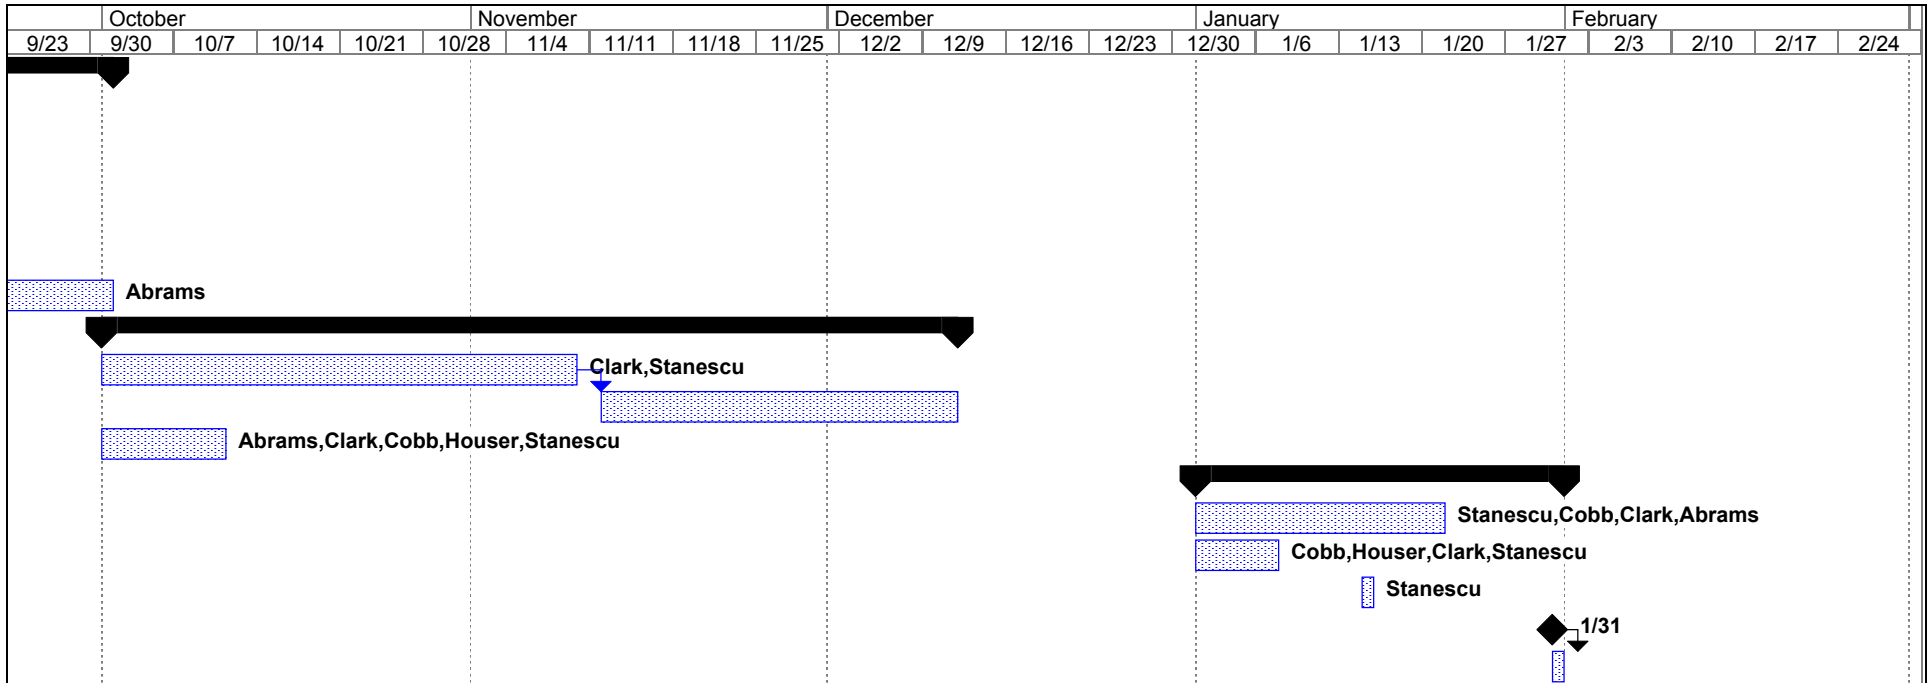9/23	October				November				December				January				February					
9/23	9/30	10/7	10/14	10/21	10/28	11/4	11/11	11/18	11/25	12/2	12/9	12/16	12/23	12/30	1/6	1/13	1/20	1/27	2/3	2/10	2/17	2/24

Project: GDFR_Initial_Schedule Date: Wed 9/13/06	Task 	Milestone 	External Tasks 
	Split 	Summary 	External Milestone 
	Progress 	Project Summary 	Deadline 



Project: GDFR_Initial_Schedule Date: Wed 9/13/06	Task 	Milestone 	External Tasks 
	Split 	Summary 	External Milestone 
	Progress 	Project Summary 	Deadline 
