


ID	Task Name	Duration	Start	September					October				Nov		
				8/20	8/27	9/3	9/10	9/17	9/24	10/1	10/8	10/15	10/22	10/29	
1	Sept 4-15	9 days	Mon 9/4/06												
2	high level reqs, use cases, domain model, d	6 days	Mon 9/4/06												
3	begin registry prototype design	3 days	Tue 9/12/06												
4	prototype database creation	8 days	Mon 9/4/06												
5	Sept 18-29	13 days	Mon 9/18/06												
6	complete component diagram	1 day	Mon 9/18/06												
7	services interfaces	2 days	Tue 9/19/06												
8	test & deploy formatregistry.org	1 day	Thu 9/21/06												
9	complete design of registry prototype	1 day	Fri 9/22/06												
10	data model design	3 days	Mon 9/25/06												
11	define distribution model	5 days	Thu 9/28/06												
12	GDFR requirements review, 1st week	5 days	Mon 9/25/06												
13	Oct 2-13	12 days	Mon 10/2/06												
14	GDFR requirements review, 2nd week	5 days	Mon 10/2/06												
15	integrate reg. prototype with SRW	3 days	Mon 10/2/06												
16	define distributed record update	4 days	Thu 10/5/06												
17	incorporate TWG proposed reqs changes	1 day	Wed 10/11/06												
18	define authentication and access control arc	3 days	Thu 10/12/06												
19	editorial process document	1 day	Tue 10/17/06												
20	CQL to xquery parser	10 days	Mon 10/2/06												
21	GDFR design reviews, 1st week	5 days	Mon 10/9/06												
22	Oct 16-27	9 days	Mon 10/16/06												
23	GDFR design reviews, 2nd week	5 days	Mon 10/16/06												
24	prototype collection UI for updates	3 days	Mon 10/16/06												
25	prototype collection UI XSL	3 days	Thu 10/19/06												
26	properties file from Collection Profile	2 days	Mon 10/16/06												
27	test SRW client search and read	2 days	Mon 10/16/06												
28	import records from Fred	2 days	Mon 10/16/06												
29	log4j and log all exceptions	1 day	Wed 10/18/06												
30	design policy 2 config distribution model	4 days	Thu 10/19/06												
31	incorporate TWG proposed design changes	2 days	Wed 10/25/06												
32	Oct 30-Nov 10	10 days	Mon 10/30/06												








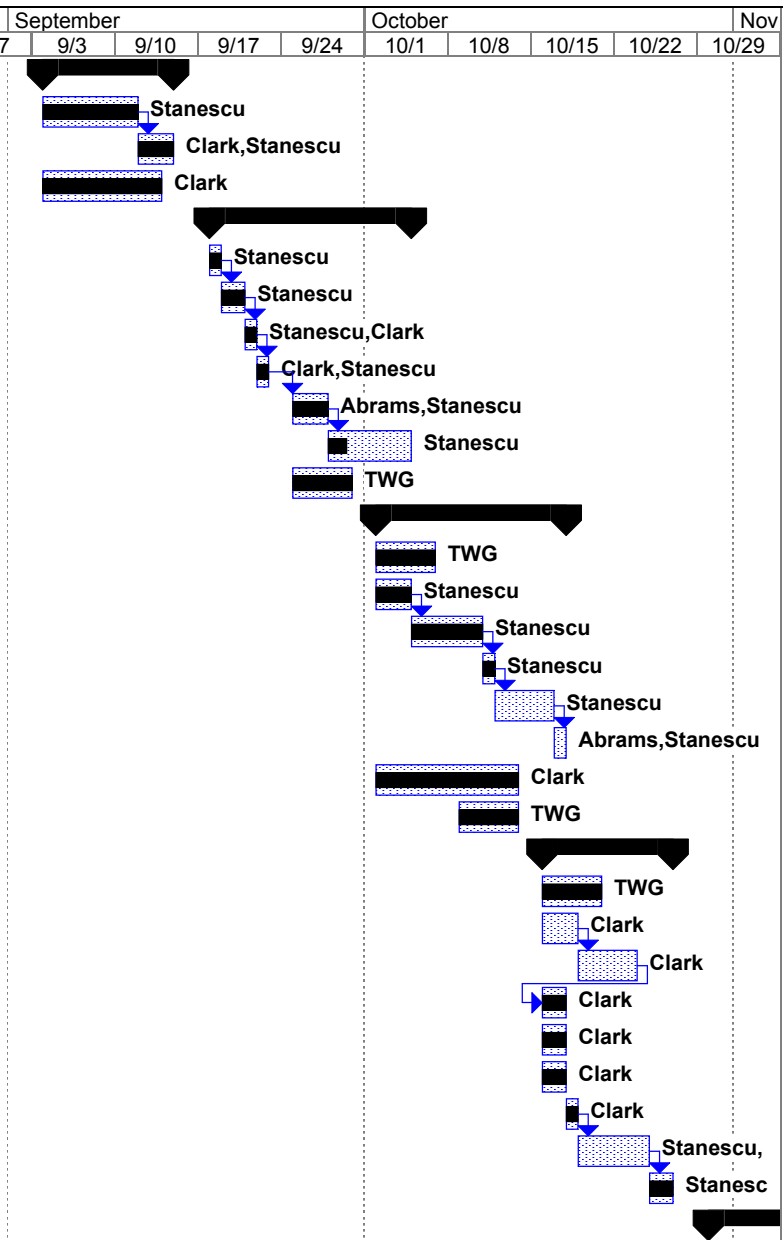



Project: GDFR_Initial_Schedule Date: Thu 11/16/06	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	

ID	Task Name	Duration	Start	September						October				Nov
				8/20	8/27	9/3	9/10	9/17	9/24	10/1	10/8	10/15	10/22	10/29
33	prepare for tech review meeting	5 days	Mon 10/30/06											
34	technical review meeting	2 days	Mon 11/6/06											
35	DLF	3 days	Wed 11/8/06											
36	Nov 13-30	14 days	Mon 11/13/06											
37	design network configuration policies	4 days	Mon 11/13/06											
38	prototype LOCKSS distribution	7 days	Fri 11/17/06											
39	prototype release and report	3 days	Tue 11/28/06											
40	prototype registry manager	8 days	Mon 11/13/06											
41	December timebox	23 days	Fri 12/1/06											
42	design inter-nodal authentication	4 days	Fri 12/1/06											
43	submit article about GDFR to DLF	3 days	Thu 12/7/06											
44	publish full specs	1 day	Tue 12/12/06											
45	publish article for DLIB	4 days	Wed 12/13/06											
46	repository integration test design	5 days	Tue 12/19/06											
47	define operations/stats requirements	5 days	Tue 12/26/06											
48	implementation platform defined	1 day	Fri 12/1/06											
49	implementation plan completed	6 days	Tue 12/26/06											
50	2nd invoice (complete specs & implementati	0 days	Tue 1/2/07											
51	registry UI design	10 days	Fri 12/1/06											
52	Jan-March 2007, Implementation	60 days	Mon 1/1/07											
53	refactor prototype as needed	15 days	Mon 1/1/07											
54	build/deploy authentication	21 days	Mon 1/1/07											
55	build UI config for inter-nodal policies	20 days	Tue 1/30/07											
56	build registry UI	25 days	Mon 1/22/07											
57	add subscribe/notify to inter-nodal logic	10 days	Tue 2/27/07											
58	integrate repository core	20 days	Mon 2/26/07											
59	April-June 2007, Interim Release	53 days	Mon 4/2/07											
60	implement operations/stats	11 days	Mon 4/2/07											
61	production packaging	15 days	Mon 4/2/07											
62	documentation for interim release	3 days	Mon 4/2/07											
63	reference model code interim release	5 days	Thu 4/5/07											
64	deploy/configure QA test envs	15 days	Thu 4/12/07											

Project: GDFR_Initial_Schedule Date: Thu 11/16/06	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	

ID	Task Name	Duration	Start	September						October				Nov	
				8/20	8/27	9/3	9/10	9/17	9/24	10/1	10/8	10/15	10/22	10/29	
65	QA test cycle at OCLC	20 days	Thu 5/3/07												
66	OCLC inter-nodel testing & bug fixing	10 days	Thu 5/31/07												
67	July-Sept 2007, Harvard test cycle	66 days	Mon 7/2/07												
68	2nd code refactor, bug fix	16 days	Mon 7/2/07												
69	2nd QA test cycle at OCLC	10 days	Tue 7/24/07												
70	3rd invoice (initial production release)	1 day	Tue 8/7/07												
71	Harvard initial install	14 days	Wed 8/8/07												
72	initial populate by Harvard staff	10 days	Tue 8/28/07												
73	Harvard inter-nodal testing	15 days	Tue 9/11/07												
74	Oct-December 2007, Pre-release	52 days	Mon 10/1/07												
75	Iterative refactoring, bug fixing	30 days	Mon 10/1/07												
76	3rd QA test cycle at OCLC	22 days	Mon 11/12/07												
77	Pre-release planning	8.4 days	Mon 10/1/07												
78	Jan-March 2008, Release	23 days?	Tue 1/1/08												
79	Turnover to external maintenance agent	15 days	Tue 1/1/08												
80	Final technical report	5 days	Tue 1/1/08												
81	Open source available	1 day	Tue 1/15/08												
82	Project end Jan 31, 2008	0 days	Thu 1/31/08												
83	4th invoice	1 day?	Thu 1/31/08												










Project: GDFR_Initial_Schedule Date: Thu 11/16/06	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	

November				December				January				February				March				April		
11/5	11/12	11/19	11/26	12/3	12/10	12/17	12/24	12/31	1/7	1/14	1/21	1/28	2/4	2/11	2/18	2/25	3/4	3/11	3/18	3/25	4/1	4/8

brams

u

Project: GDFR_Initial_Schedule
Date: Thu 11/16/06










Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	


November				December				January				February				March				April		
11/5	11/12	11/19	11/26	12/3	12/10	12/17	12/24	12/31	1/7	1/14	1/21	1/28	2/4	2/11	2/18	2/25	3/4	3/11	3/18	3/25	4/1	4/8

Project: GDFR_Initial_Schedule
Date: Thu 11/16/06


Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

4/15			May				June				July				August				September			
4/15	4/22	4/29	5/6	5/13	5/20	5/27	6/3	6/10	6/17	6/24	7/1	7/8	7/15	7/22	7/29	8/5	8/12	8/19	8/26	9/2	9/9	9/16



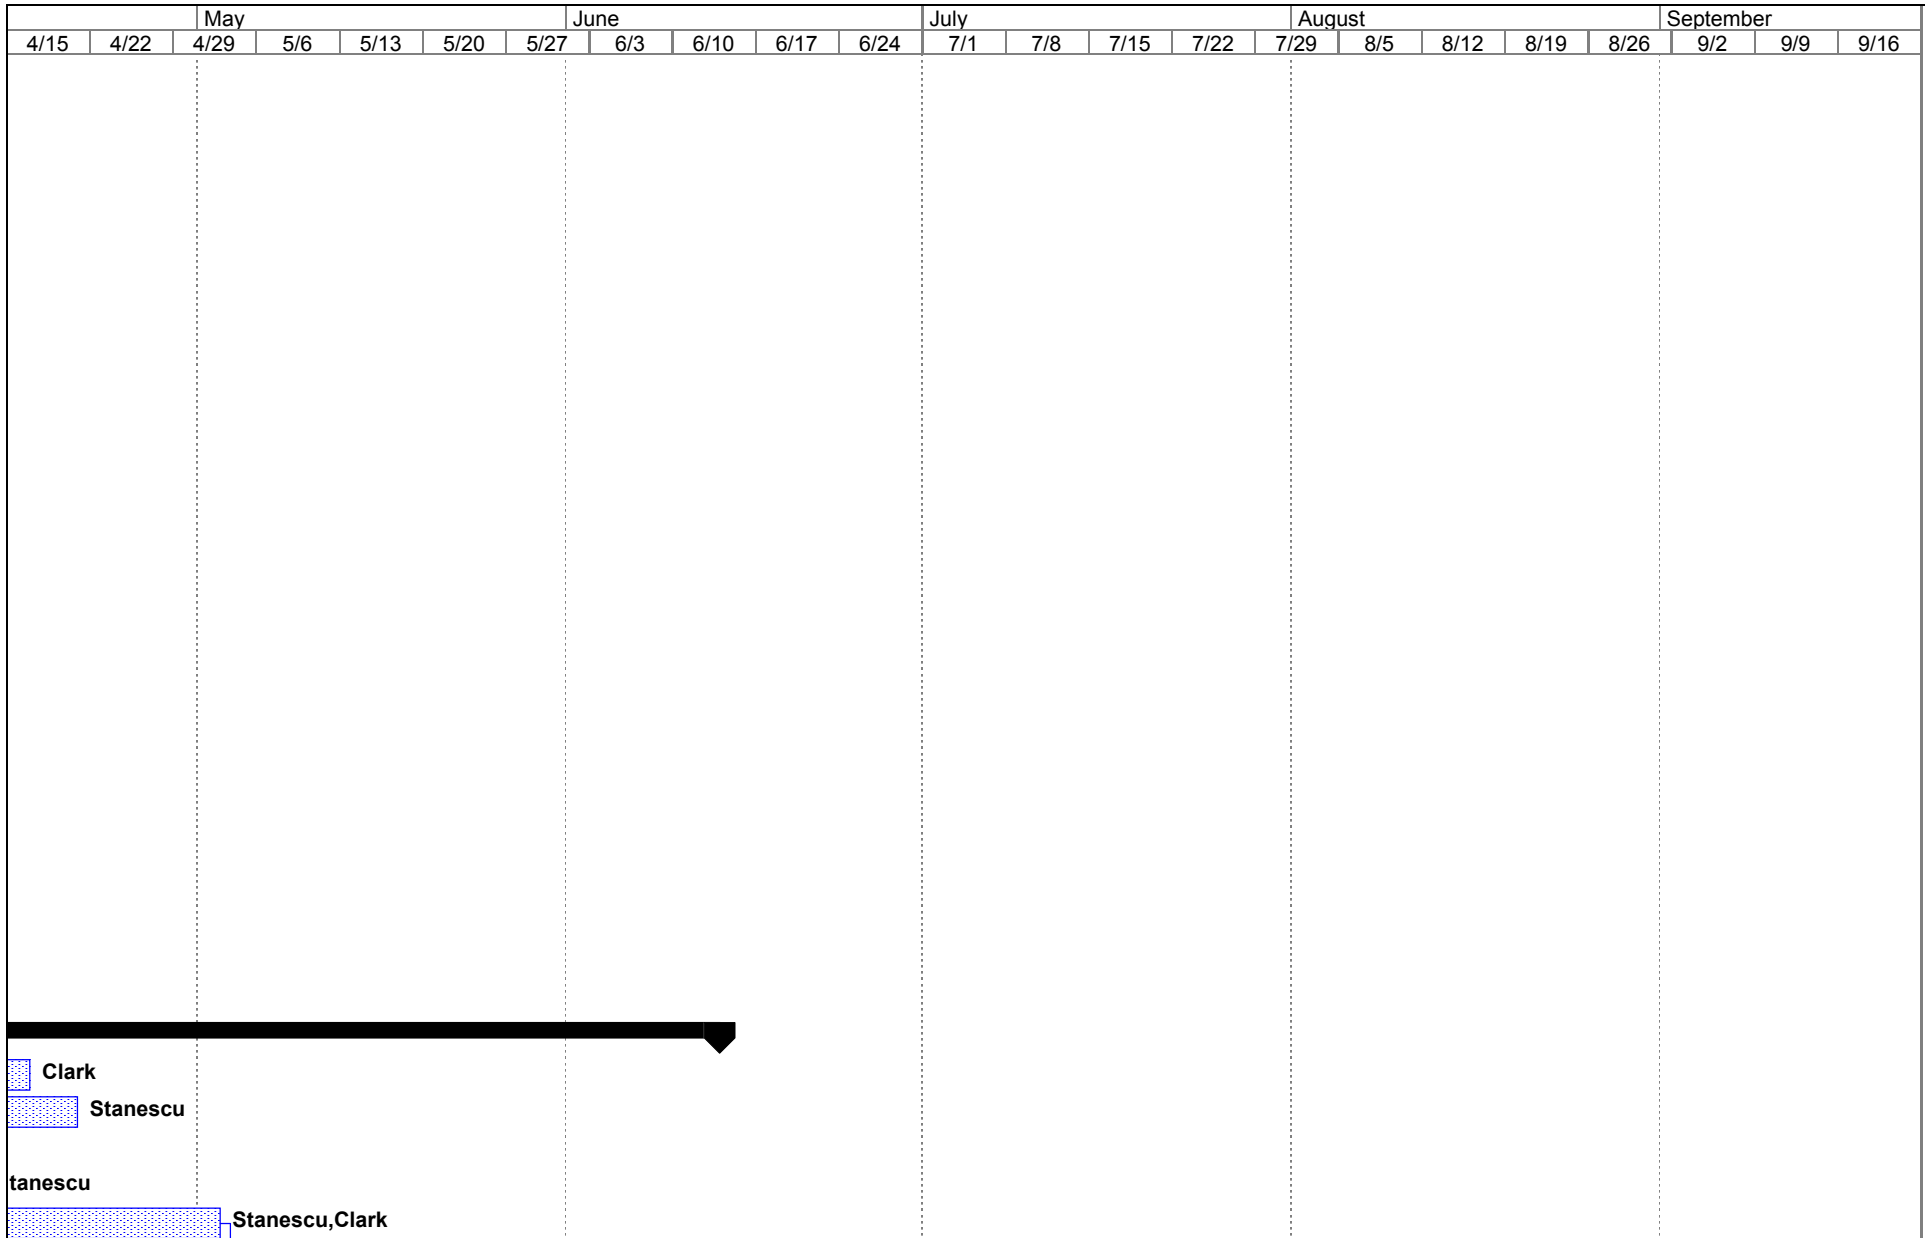

Project: GDFR_Initial_Schedule Date: Thu 11/16/06	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	

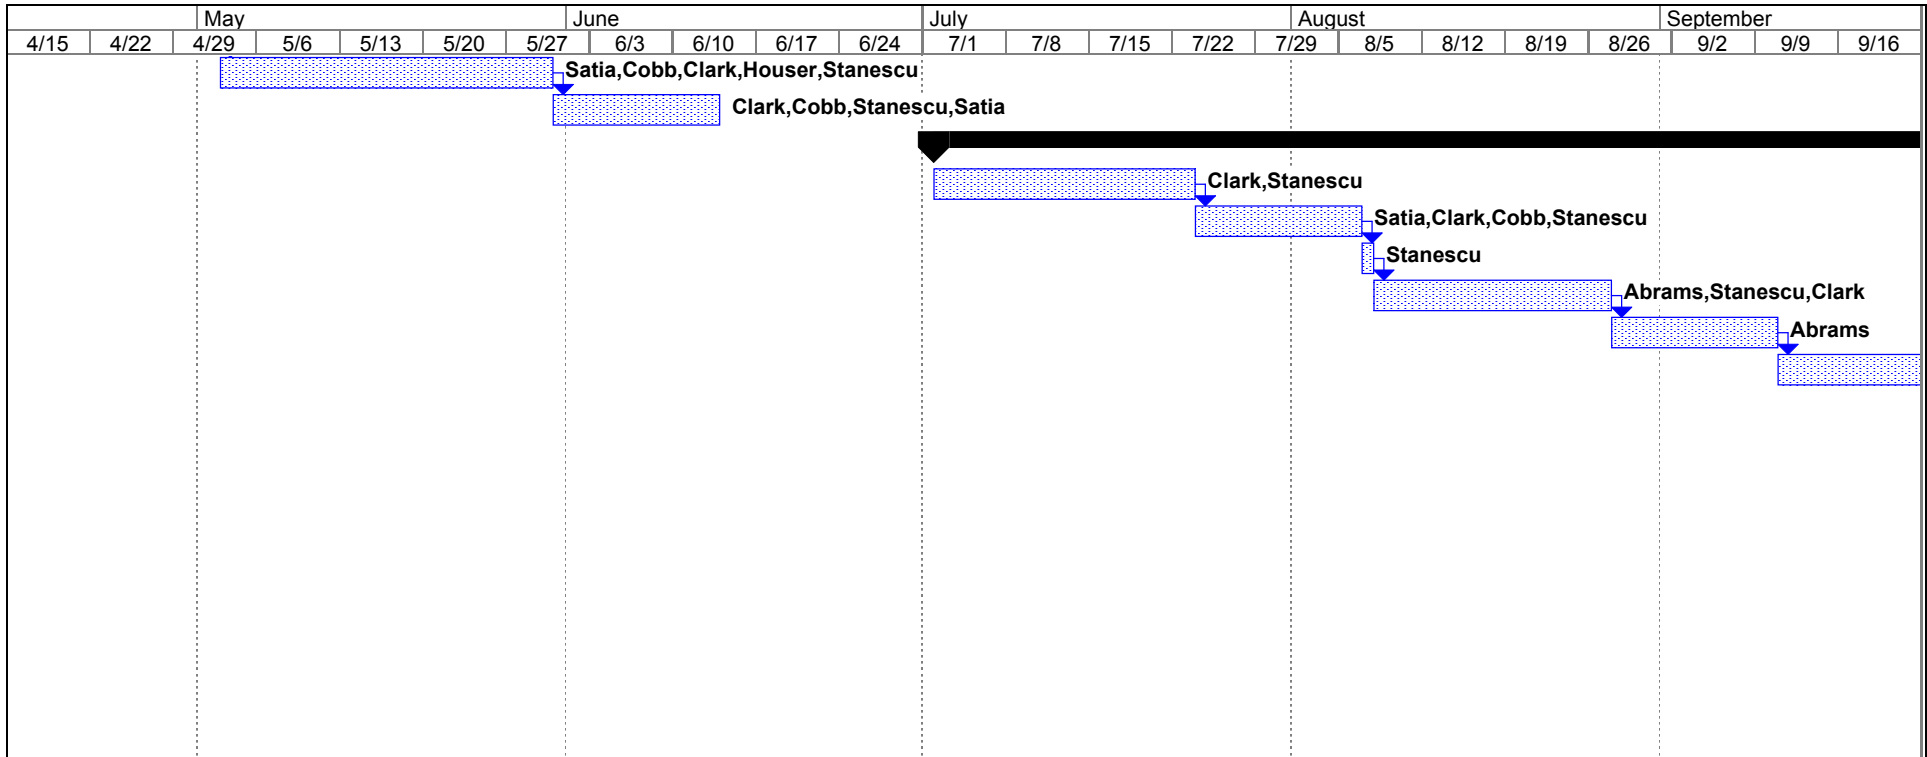










Project: GDFR_Initial_Schedule Date: Thu 11/16/06	Task	Milestone	External Tasks
Split	Summary	External Milestone	Deadline
Progress	Project Summary		












Project: GDFR_Initial_Schedule
 Date: Thu 11/16/06


Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

9/23	October				November				December				January				February					
9/23	9/30	10/7	10/14	10/21	10/28	11/4	11/11	11/18	11/25	12/2	12/9	12/16	12/23	12/30	1/6	1/13	1/20	1/27	2/3	2/10	2/17	2/24

Project: GDFR_Initial_Schedule Date: Thu 11/16/06	Task 	Milestone 	External Tasks 
	Split 	Summary 	External Milestone 
	Progress 	Project Summary 	Deadline 

9/23	October				November				December				January				February					
9/23	9/30	10/7	10/14	10/21	10/28	11/4	11/11	11/18	11/25	12/2	12/9	12/16	12/23	12/30	1/6	1/13	1/20	1/27	2/3	2/10	2/17	2/24

Project: GDFR_Initial_Schedule Date: Thu 11/16/06	Task 	Milestone 	External Tasks 
	Split 	Summary 	External Milestone 
	Progress 	Project Summary 	Deadline 

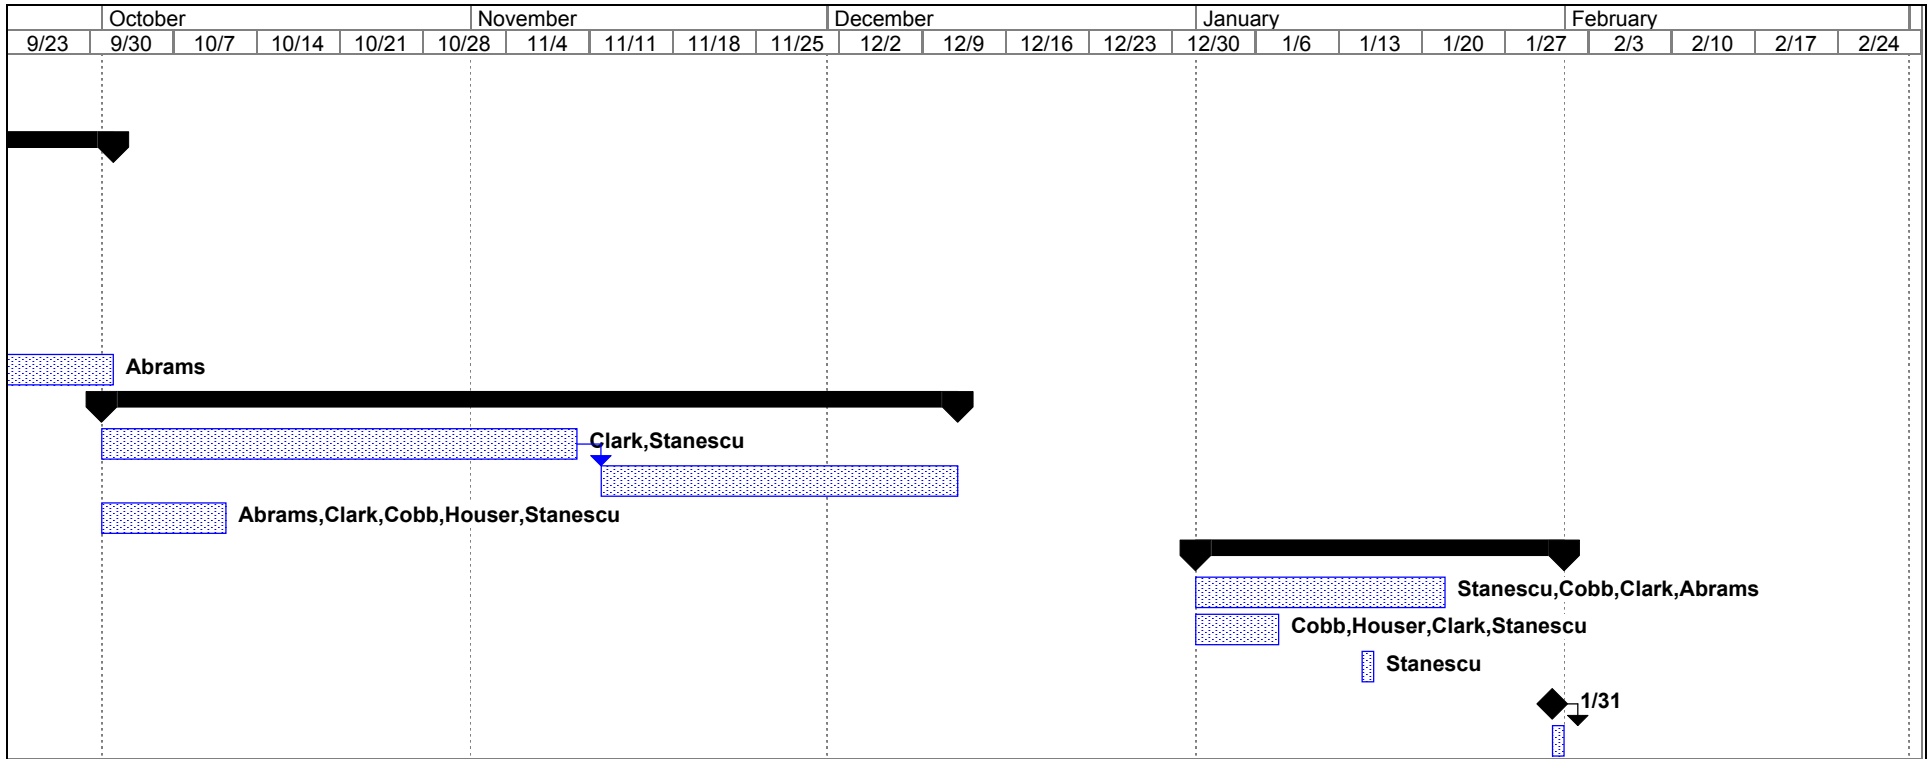

Project: GDFR_Initial_Schedule
 Date: Thu 11/16/06

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	
